



**PROJECT NAME:** Beachfront RV Park Improvements / Port of Brookings-Harbor  
**PROJECT #:** 19005

**Addendum No. 2 for Beachfront RV Park Improvements**

The original Drawings and Specifications dated August 2021, are hereby modified and supplemented by this Addendum No. 2 dated September 23, 2021.

**QUESTIONS FROM CONTRACTORS**

- Can native soils be used to backfill utility trenches?  
Answer: No, see Utility Trench Details attached.
- On sites 33 thru 38, can native soils be used up to 6" from finish grade?  
Answer: No, use gravel paving base coarse aggregate - 1-1/2" minus.

**CLARIFICATION:** Utility Trench Details attached.

END OF ADDENDUM NO. 2



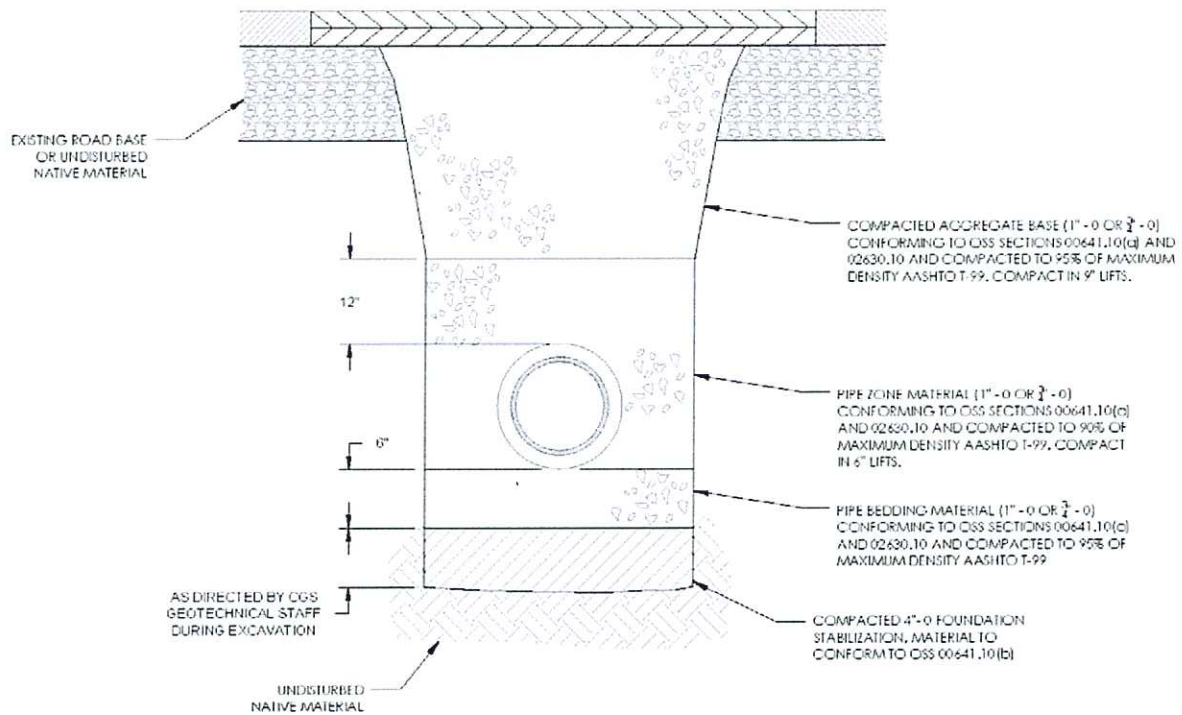


Figure 2 - Trench in ROW, Under Structure or Pavement, Etc.

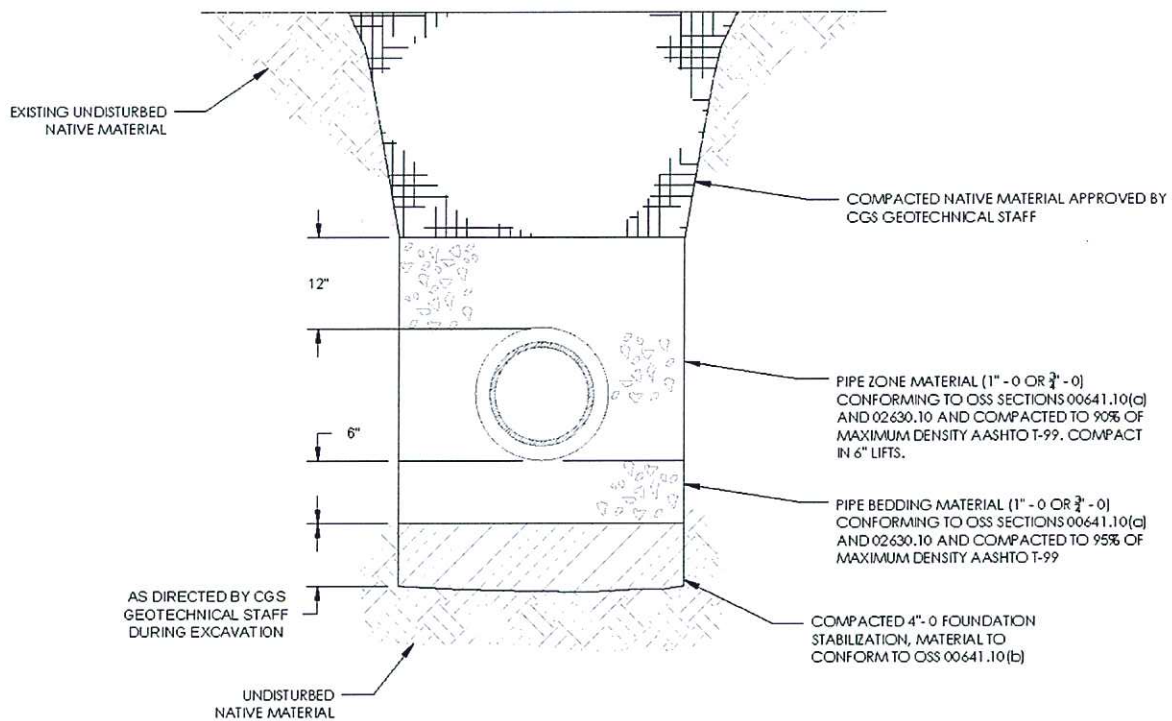


Figure 3 - Trench Not in ROW, Under Structure or Pavement, Etc.
